Commercial Contractors L.P.

Smith Interior Remodel

Job No.: 980045.05 Cmpl.: 08/23/2
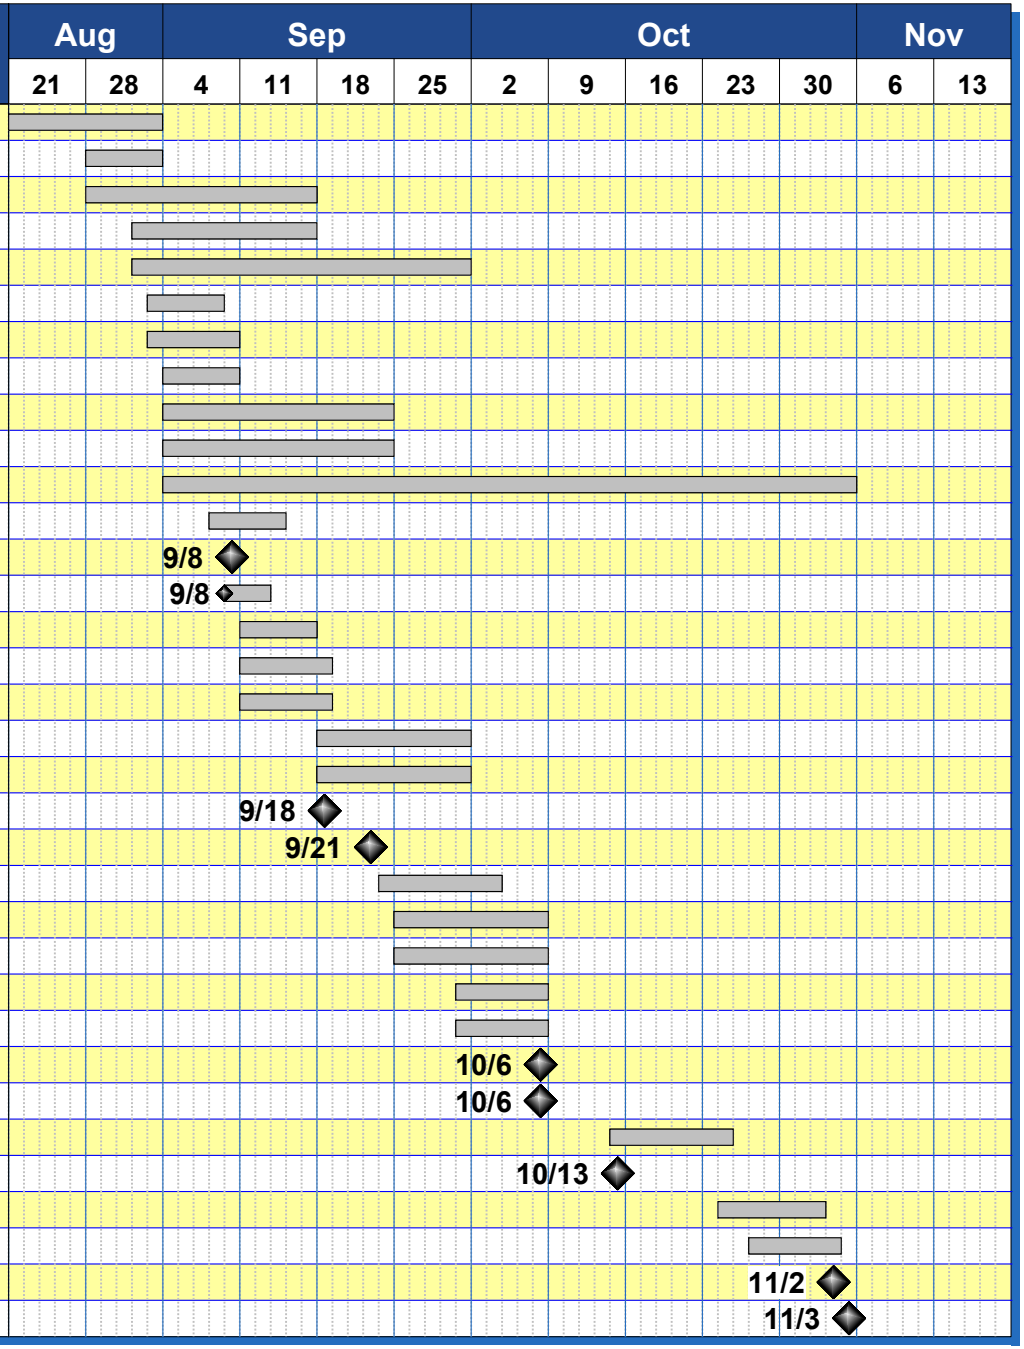
	Start	Finish
Soft Demo	8/21	9/1
Sawcut & Demo-Structural	8/28	9/1
Structural Steel-Fab	8/28	9/15
Framing-Rough	8/31	9/15
HVAC-Rough	8/31	9/29
Wall Saw & Demo	9/1	9/7
Structural Concrete-Rebar	9/1	9/8
HVAC-Curbs/Platforms	9/4	9/8
Skylights	9/4	9/22
Roofing Curbs & Patch	9/4	9/22
Electrical-Rough/Finish	9/4	11/3
Overhead Doors	9/7	9/13
Inspection-Structural Rebar	9/8	9/8
Structural Concrete-Pour	9/8	9/12
Service/Repair Elevator	9/11	9/15
Plumbing Rough	9/11	9/18
Data/Phone Cableing	9/11	9/18
Structural Steel-Install	9/18	9/29
T-bar Grid Repair	9/18	9/29
Inspection-Walls	9/18	9/18
Inspection-Drywall Screw	9/21	9/21
Mud & Tape	9/22	10/3
Mezzanine Demo	9/25	10/6
Structural Steel Handrail	9/25	10/6
Electrical-Buss Duct	9/29	10/6
Doors/Frame/Hardware	9/29	10/6
Spiveco Equip Move-In	10/6	10/6
T.C.O. from City	10/6	10/6
Ceiling Tile	10/13	10/24
Inspection-Ceiling	10/13	10/13
Paint	10/24	11/1
Carpet	10/26	11/2
Inspection-Elec, Mech & Fire	11/2	11/2
Inspection-Building Final	11/3	11/3
